

ITS Communications & Wireless LMR System Replacement SIEC Update

Tim McDowell ITS Communications Manager

Dongho Chang Director Traffic Operations

October 25, 2021

Roger Millar, Secretary of Transportation

Amy Scarton, Deputy Secretary of Transportation

Progress to date





Project Status

- Final project completion has shifted due to site lease issues and micro possessor availability impacting equipment delivery. The Project team will be evaluating the schedule and completion of all project tasks in November. New estimated completion date is summer of 2022.
- 130 of the 136 sites statewide are installed and operational.
- North Central (NCR), Olympic (OR), Southwest (SWR) and South Central (SCR) regions.

 Eastern (ER) region has 2 site that are pending complete. The remaining 4 sites will be completed at the end of the project and are considered coverage improvement sites but not critical to operations.
- Subscriber installs are completed in NWR and NCR, OR and SCR installs are underway. SWR and ER pending completion in OR and SCR.

Upcoming tasks







- Maintain OCIO IT Pool Dashboard
 - Scope



Schedule




Budget



OCIO Assessment (A)




- Update schedule with new project completion date, update OCIO Technology Budget.
- Current status and quality assurance reports are on the OCIO dashboard.
- Complete coverage testing in SWR and ER and complete install final 2 site in ER.
- Continue subscriber installs in OR and SCR. SWR and ER subscriber installs pending OR and SCR completion.
- System Final Acceptance in December.

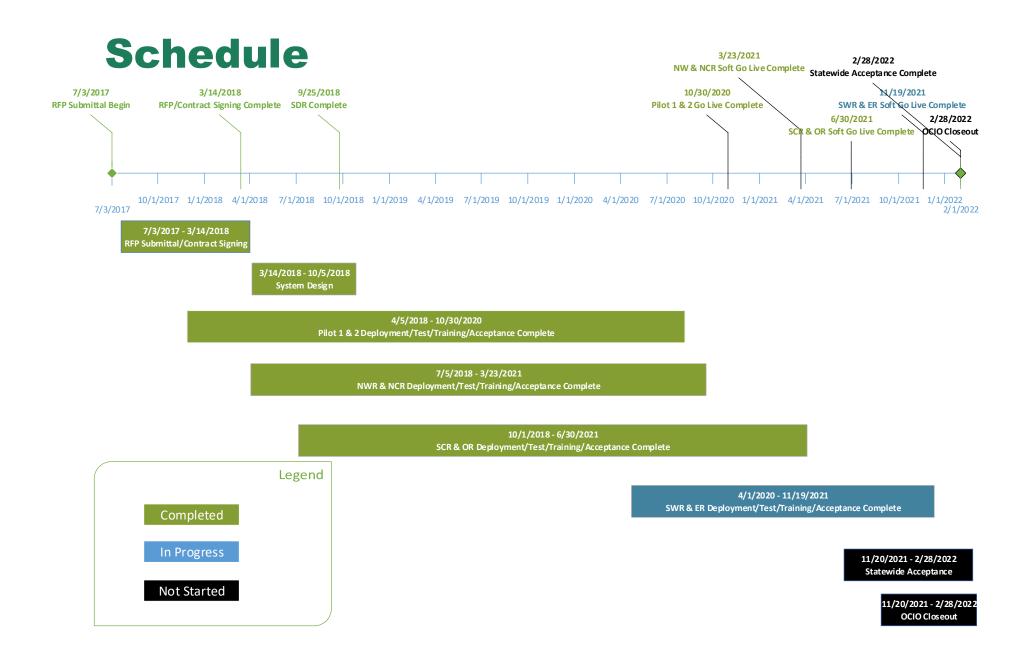

Schedule

90 Day Tasks

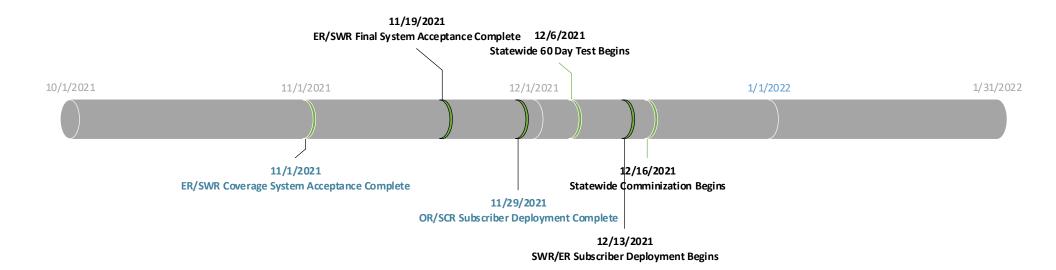

Questions?

