

ITS Communications & Wireless LMR System Replacement SIEC Update

Tim McDowell ITS Communications Manager

John Nisbet Director Traffic Operations

June 20, 2019

Roger Millar, Secretary of Transportation

Keith Metcalf, Deputy Secretary of Transportation

Progress to date





- FCC licensing is complete.
- First milestone system design review is complete.
- OCIO security design review is complete and approved.
- Schedule shifted during system design review.
- Some pilot and regional deployment activities are compressed to meet the agency goal of completing 2 regions before December of 2019. Mainly to ensure we have spare parts going into that winter season.
- Final region complete is still December of 2021
- Primary system cores are installed.
- Pilot site installs for Northwest Region and North Central are underway.
- Factory acceptance fro Northwest and North Central is complete

Upcoming tasks





- Maintain OCIO IT Pool Dashboard
 - Scope



Schedule



Budget




OCIO Assessment



- Current status and quality assurance reports on the OCIO Dashboard.
- Complete detailed design for Northwest and North Central regions.
- Install equipment for pilot and conduct pilot testing.
- Delivery of remaining sites in Northwest and North Central regions and install equipment.
- Complete detailed design review for South Central and Olympic regions.


Schedule

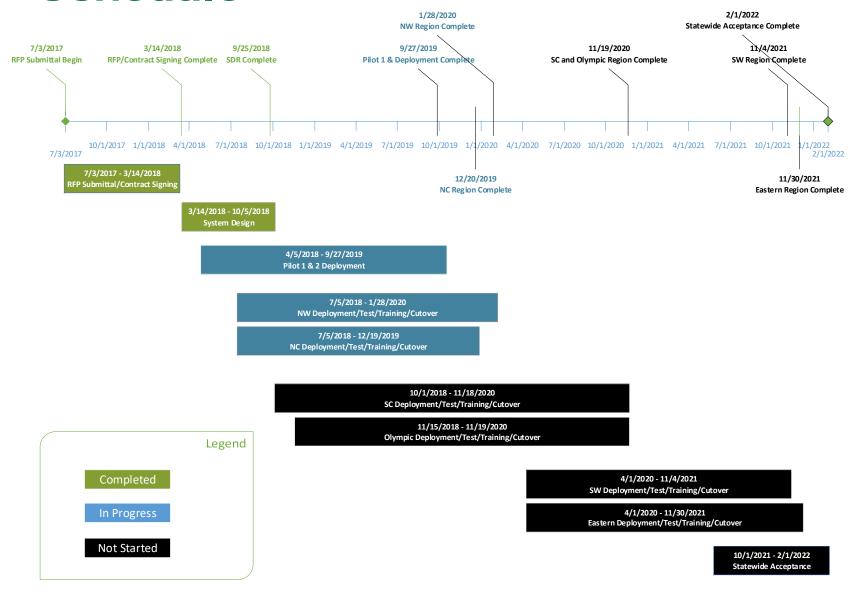



Schedule

90 Day Tasks

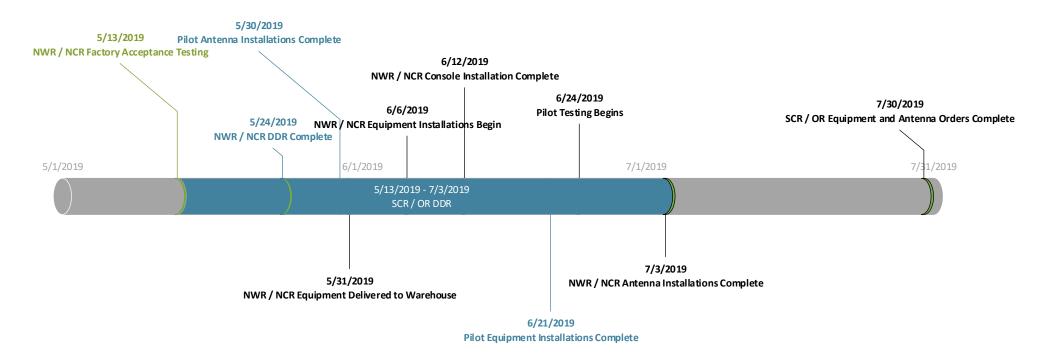



Questions?

