

ITS Communications & Wireless LMR System Replacement

SIEC Update

Tim McDowell
ITS Communications Manager

Ron Vessey
Acting - Director Traffic Operations

August 15, 2020

Roger Millar, Secretary of Transportation

Keith Metcalf, Deputy Secretary of Transportation





Progress to date



- Project Status
 - Schedule has shifted due to COVID-19, overall impact of the delays will not be known until the 2020/2021 winter season shuts down construction activities. Overall schedule to complete is still scheduled for December of 2021.
 - Low Risk and Medium risk activities have restarted, Harris is providing weekly update on COVID planning.
 - Pilot Coverage testing is complete. Compiling data and reviewing reports.
 - Site work is near complete in Northwest (NWR) and North Central (NCR) Regions. Olympic (OR) and South Central (SCR) regions have started construction work and are planned to be complete November of 2020.
 - System acceptance for NWR and NCR was accepted this month, and project is now completing coverage testing.
 - Mobile installs for NWR and NCR will be scheduled for fall of 2020.
 - Completed Detailed Design for Eastern and Southwest Regions.


Upcoming tasks



- Maintain OCIO IT Pool Dashboard
 - Scope 
 - Schedule 
 - Budget 
 - OCIO Assessment 
- Update OCIO investment plan to reflect new monthly expenditures due to COVID delays.
- Current status and quality assurance reports on the OCIO Dashboard.
- Complete coverage testing in NWR and NCR and complete pilot testing.
- Continue site installs in OR and SCR.
- Finalize training material.
- Update schedule to reflect impacts of COVID-19 once winter season has shut down site installs.



Schedule

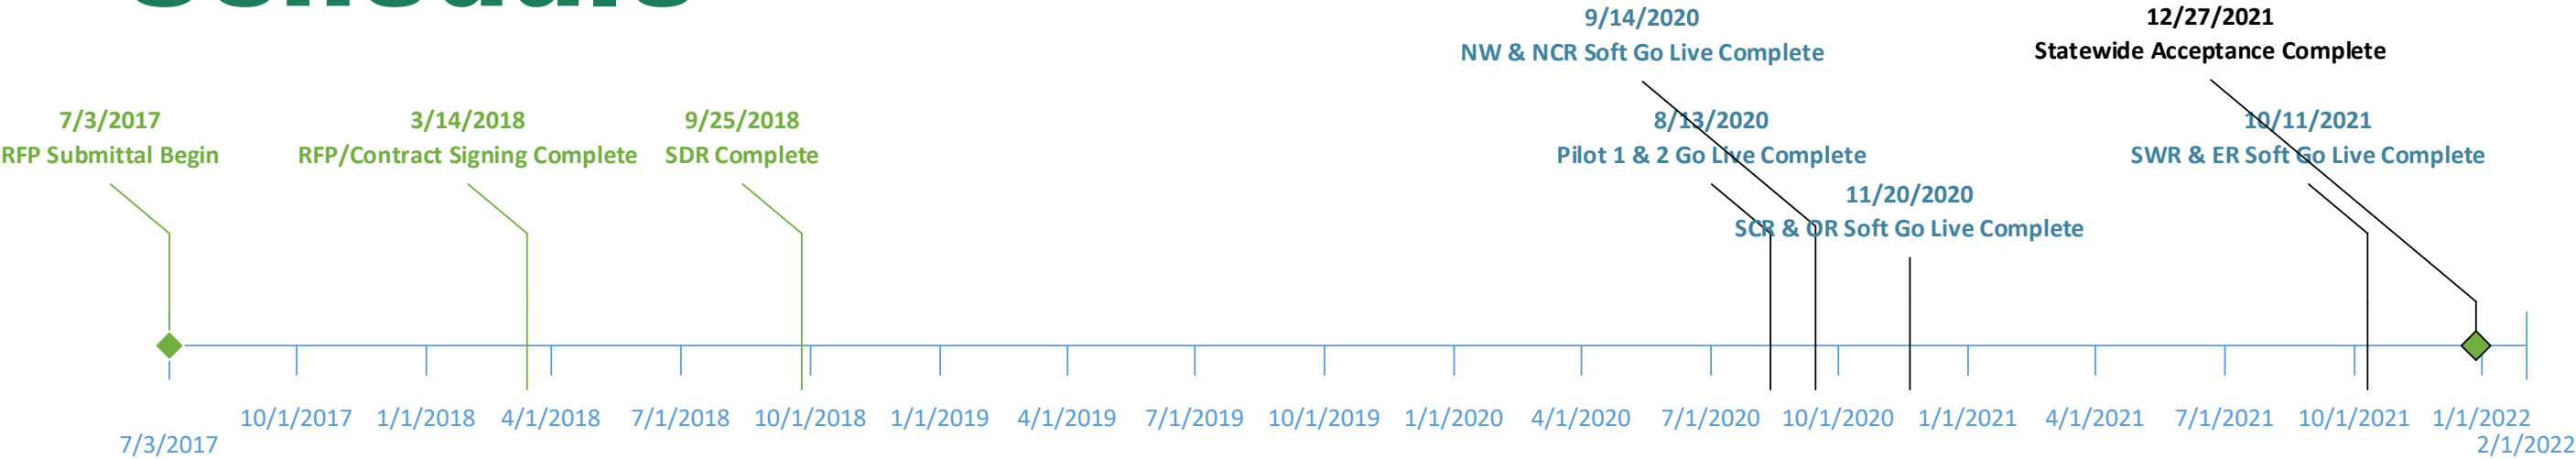

7/3/2017 - 3/14/2018
RFP Submittal/Contract Signing

3/14/2018 - 10/5/2018
System Design

4/5/2018 - 5/18/2020
Pilot 1 & 2 Deployment/Test/Training/Acceptance Complete

7/5/2018 - 6/12/2020
NWR & NCR Deployment/Test/Training/Acceptance Complete

10/1/2018 - 9/29/2020
SCR & OR Deployment/Test/Training/Acceptance Complete

4/1/2020 - 10/11/2021
SWR & ER Deployment/Test/Training/Acceptance Complete

10/1/2021 - 12/27/2021
Statewide Acceptance


Legend

- Completed
- In Progress
- Not Started

Schedule doesn't reflect COVID-19 delays

Schedule

90 Day Tasks

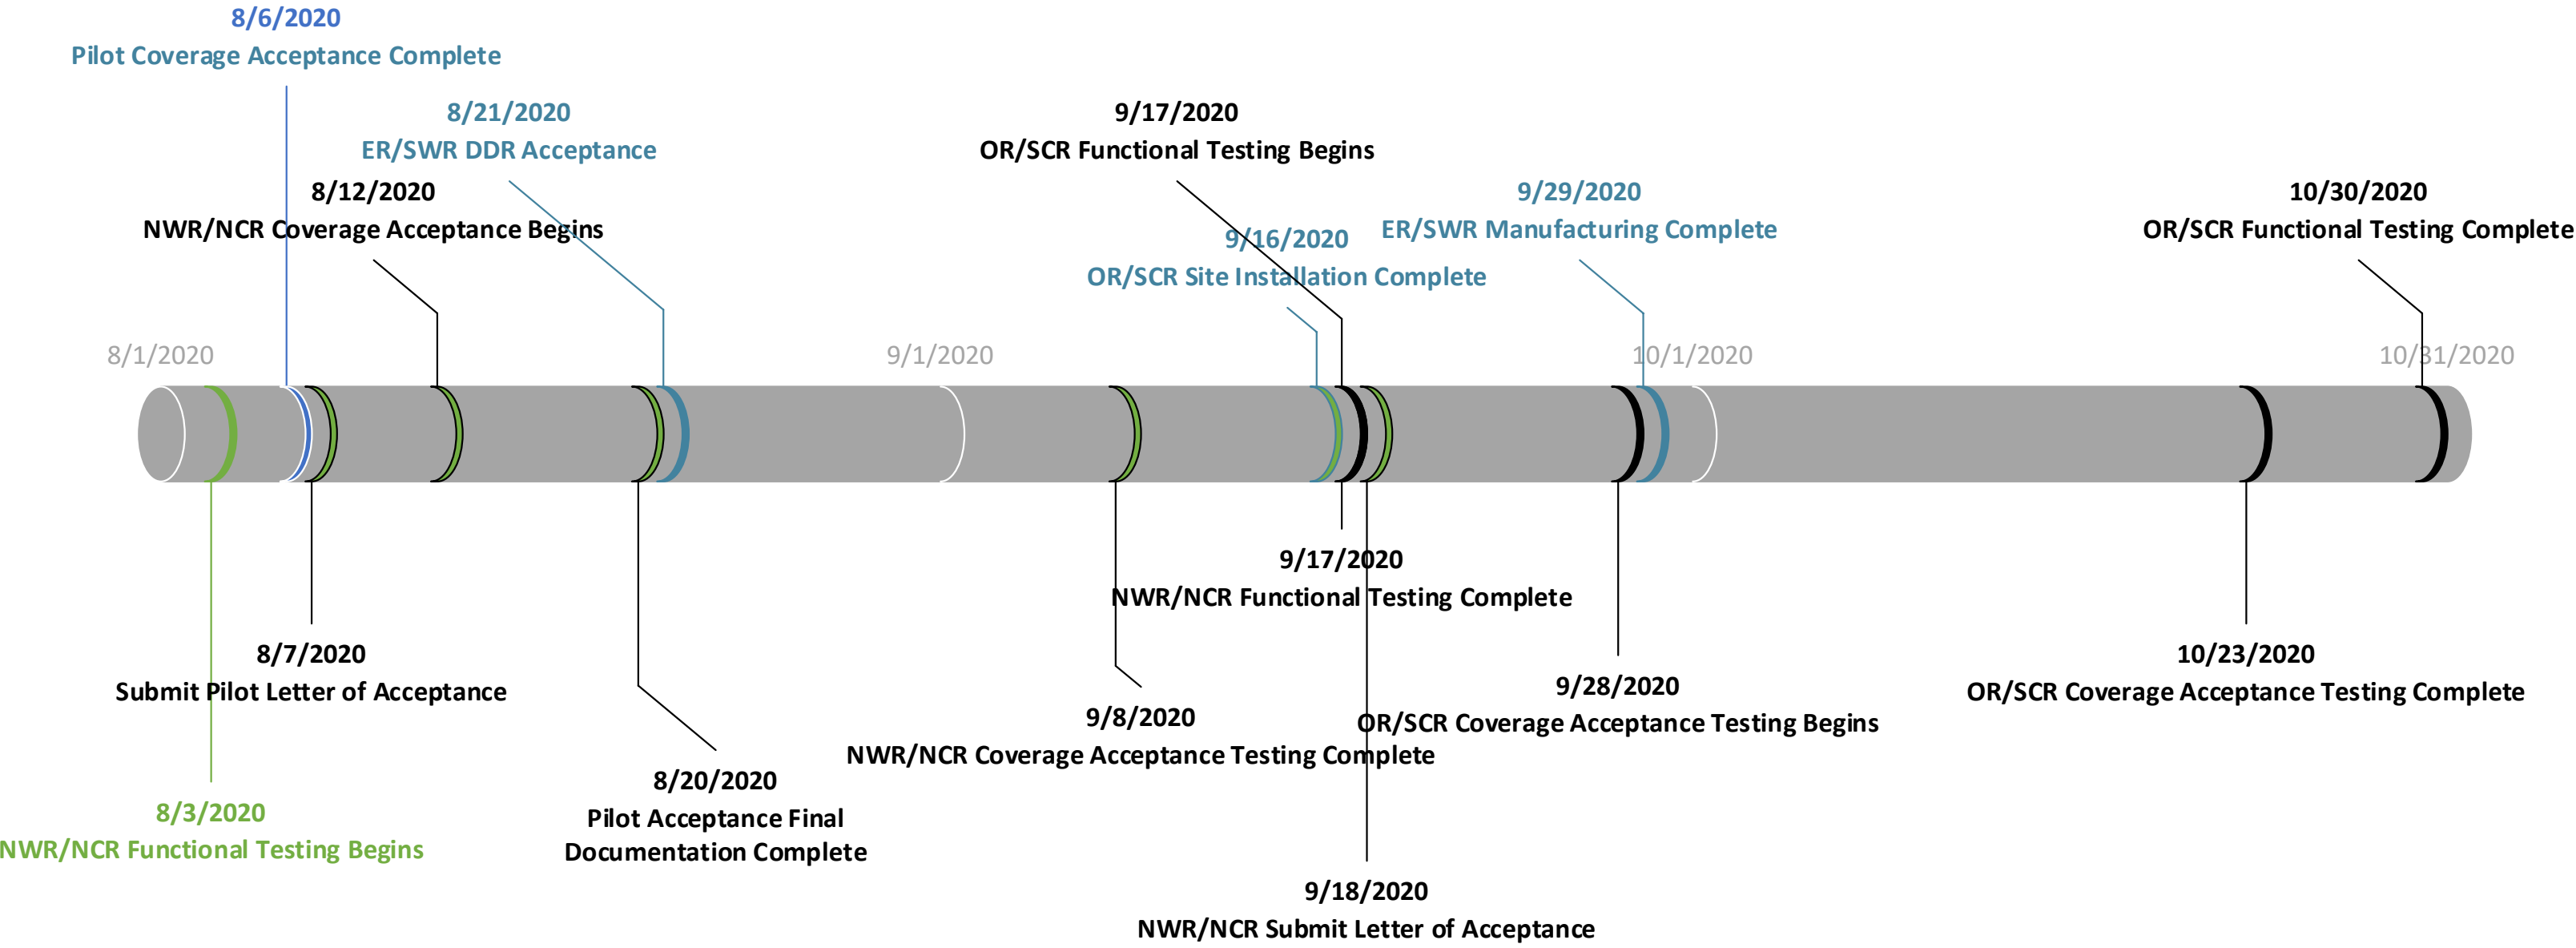

Questions?

Tim McDowell
Washington State Department of Transportation
ITS Communications & Wireless Technology
mcdowet@wsdot.wa.gov
(360)705-7028

