

PILOT REMEDIATION

TUE 11/15/16 - FRI 7/14/17

% COMPLETE

44%

PROJECT MILESTONE DATES

Project Milestones with planned finish date and the current completion percentage for resolution of prioritized gaps by Pillar and for Campus Solutions: Pillar/Module.


Name	% Complete	Finish
Remediation Plan	44%	Fri 7/14/17
Critical Gaps	56%	Fri 7/14/17
HCM	49%	Fri 7/14/17
CS: Core	61%	Fri 7/7/17
CS: Student Financials	98%	Wed 5/10/17
CS: Financial Aid	57%	Wed 6/7/17
FIN	54%	Fri 6/16/17
Cross-Pillar: HCM-FIN	19%	Thu 6/15/17
Urgent Gaps	18%	Wed 7/12/17
HCM	14%	Tue 6/13/17
CS: Core	50%	Tue 6/27/17
FIN	9%	Wed 7/12/17
High Gaps	18%	Thu 7/6/17
HCM	0%	Wed 6/28/17
CS: Core	36%	Mon 7/3/17
CS: Student Financials	23%	Thu 7/6/17
CS: Financial Aid	78%	Mon 5/8/17
FIN	0%	Tue 6/27/17

* Project Dashboard %Complete revised for Additional A/R Task Detail.

** Ticket Metrics revised for accuracy.

% COMPLETE AS OF - 5/1/2017

Overall Status for all top-level tasks, Critical Urgent and High gap resolution for all pillars/modules.

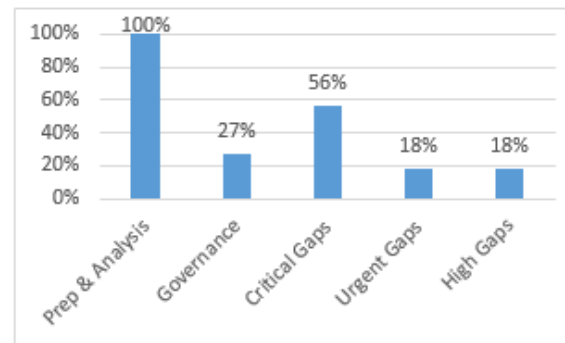

TOP PRIORITY RISKS

#99 - Resources for FY16/FY17 Year-End Close Affecting Remediation:

PROBABILITY: DEFINITE **IMPACT:** HIGH

Risk: Possible 6 week delay in closure of Remediation for Finance.

Insufficient resources in Finance ERP Support to provide production support and significant additional work for closing both FY16 & FY17. Resource constraints will impact Remediation Team, risking remediation task timeline. Remediation Team resources have been diverted to assist FY16 close on-site activities, general support assistance and participation in Common Process Development workshops. Resource drain will worsen as the FY17 year-end close deadline nears.

TOP PRIORITY ISSUES

#411 - Hyperion Decision - Budget Requirements for Hyperion Remain Unmet:

A decision is needed to either staff the Hyperion solution or opt for an alternate approach\tool to meet these requirements. Impacts Budget Development & Planning.

#412 - Online Admissions Application (OAA) - Citizenship, Residency & Phone Number:
-Blank citizenship status, Running Start programs want residency questions, Spokane wants phone number to be required, TCC has objections about this request.

#413 - Payroll Deduction Liability Account Changes Needed:

Need global college workgroup to establish new Payroll Deduction Liability Accounts.

#414 - Continued lack of FWL ERP Support Resource Impacting Remediation:

ERP Support has not hired a resource to support Faculty Workload. Project resource providing all support for FWL impacting Remediation. Most notably: FWL Routing for Contract Approval Multi-Meeting Pattern Fix for FWL Calculation Control Roll-Forward Fix These issues are on the critical path for closure of Remediation.

TICKETS TO DATE: Total Closed [ALL]: 537 Total [REM]: 337 Open [REM]: 290 Closed [REM]: 47

Critical Total : 50 Closed: 13 Open: 37 Pending Governance: 1

Urgent Total : 71 Closed: 12 Open: 47 Pending Governance: 0

High Total : 217 Closed: 22 Open: 195 Pending Governance: 6

Total Low\Medium Priority Tickets Deferred to Wave Deployments: 1,217

Medium Total : 110 Closed: 22 Open: 97 Pending Governance: 3

Low Total : 2040 Closed: 478 Open: 1563 Pending Governance: 440

CEMLI STATUS DASHBOARD

PILLAR	NAME	START	FINISH	% COMPLETE
CS:FA	SNG HOUSEHOLD SIZE FIX (E-008)	MON 12/19/16	FRI 2/10/17	100%
CS:FA	SNG ARCHIVE PAGE (E-008)	MON 4/10/17	WED 6/7/17	12%
FSCM	FINANCE IPEDS REPORTING (R-088A TO R-088F)	TUE 11/15/16	MON 5/22/17	56%
FSCM	AFRS REPORTING (I-013)	FRI 1/20/17	WED 6/7/17	31%
FSCM	STATE AUDITORS OFFICE REPORTING (I-083)	TUE 12/13/16	THU 5/11/17	86%
HCM	BALLOON PAYMENT (SE-223)	TUE 11/15/16	TUE 5/2/17	100%
HCM	BENEFIT ENTITLEMENT (PTF BEN ELIG E-031)	TUE 11/15/16	THU 5/18/17	83%
HCM	HOURLY RATE OF PAY\LWO\OT CALC (SE-219)	MON 3/27/17	THU 6/15/17	35%
HCM	JOB END DATE/PAYROLL STATUS (SE-224)	THU 3/23/17	THU 5/11/17	50%
HCM	DEPARTMENT TERM SUMMARY\EARN CODE FIX (E-022)	WED 1/18/17	WED 3/15/17	100%
HCM	SIMPLIFY PROCESS (ROUTING\CONTRACT REDO) (E-027)	THU 4/6/17	FRI 7/14/17	0%
HCM	MULTI-MEETING PATTERN DEFECT (E-023)	TUE 3/21/17	WED 5/24/17	0%
FSCM	GLE ANALYSIS TYPE CEMLI FOR PAYROLL (SE-???)	THU 5/4/17	FRI 6/9/17	0%

CONFIGURATION STATUS DASHBOARD

PILLAR	NAME	START	FINISH	% COMPLETE
CS:SF	COLLECTIONS CONFIGURATION	MON 2/13/17	THU 7/6/17	12%
CS:SF	BASIC SKILLS CONFIGURATION	WED 3/22/17	THU 6/1/17	34%
HCM	CONTRACT ADMINISTRATION CONFIGURATION (IF APPLICABLE)	THU 5/11/17	FRI 6/23/17	0%
FSCM	COST SHARING PROJECT/GRANTS	MON 5/22/17	TUE 6/27/17	0%
PILLAR	NAME	START	FINISH	% COMPLETE
HCM	W2 CONFIGURATION	WED 3/15/17	WED 5/10/17	63%
HCM	SHIFT DIFFERENTIAL RULES CONFIGURATION	TUE 3/21/17	TUE 5/9/17	6%
CS:FA	COLLEGE BOUND SCHOLARSHIP EQUATION ENGINE	TUE 4/4/17	TUE 5/16/17	50%
CS	OAA APPLICATION COMPLETION ISSUES	THU 4/20/17	FRI 7/7/17	21%

TRAINING MATERIAL AND DELIVERY STATUS DASHBOARD

PILLAR	NAME	START	FINISH	% COMPLETE
HCM	ARREARS AND SUSPENDED DEDUCTIONS	THU 4/20/17	MON 5/15/17	9%
HCM	SEPARATED EMPLOYEES (PAYABLE TIME)	TUE 4/25/17	MON 5/22/17	0%
HCM	CHECK REVERSAL VENDOR PAYMENTS	FRI 4/7/17	FRI 4/14/17	100%
HCM	EMPLOYEES WITH DISABILITIES	WED 3/22/17	MON 4/17/17	100%
HCM	EMPLOYEES ON WORK VISAS	FRI 3/24/17	MON 3/27/17	100%
HCM	TRACKING DEGREE INFO FOR EMPLOYEES	WED 3/15/17	TUE 5/9/17	81%
HCM	HCA INTERFACE	WED 3/29/17	MON 4/3/17	100%
HCM	METLIFE INTERFACE	THU 3/30/17	MON 4/3/17	100%
HCM	DRS HOURS REPORTING (FTF)	FRI 3/31/17	TUE 4/4/17	100%
HCM	ADDITIONAL BENEFIT TRAINING MATERIALS	WED 3/29/17	TUE 4/11/17	100%
FSCM	TRACK & MAINTAIN BUDGETS	WED 5/31/17	TUE 6/13/17	0%
FSCM	BUDGET INQUIRY & REPORTING	MON 6/12/17	MON 6/19/17	0%
PILLAR	NAME	START	FINISH	% COMPLETE
CS	NATIONAL STUDENT CLEARINGHOUSE	THU 2/23/17	THU 5/4/17	99%
CS	FACILITY CONFLICT NOTIFICATION	WED 3/8/17	FRI 5/19/17	36%
CS:FA	STUDENT DOCUMENT UPLOAD/DOWNLOAD	TUE 3/21/17	MON 5/8/17	78%
CS:SF	SWAP FUNCTION	TUE 11/15/16	FRI 5/5/17	8%
FSCM	AR BILLING	WED 5/24/17	WED 6/14/17	0%
PILLAR	NAME	START	FINISH	% COMPLETE
CS	RECRUITING & ADMISSIONS	THU 4/20/17	WED 6/14/17	22%
CS	CHECKLISTS & COMMENTS	TUE 5/2/17	WED 6/14/17	42%
CS	CURRICULUM MANAGEMENT	FRI 2/3/17	THU 5/25/17	33%
CS	STUDENT RECORDS	MON 3/27/17	THU 6/8/17	28%
